

LTP Steering Group 15

29 October

Agenda – 4.5hr meeting

Item	Owner	Time
1. Capital programme	Jesse, Simon	2hrs 15mins 12-2:15pm
Break		2:15-2:45pm
2. Alternative funding	Pennie, Natalie, Jesse	45mins 2:45-3:30pm
3. Activity Management Plans and KPIs	Caleb	30mins 3:30-4pm
4. RAS proposal	Katherine	25mins 4-4:25pm
5. Steering Group work programme	Caleb	5 mins 4:25-4:30pm

Capital programme

Capital programme development

STEERING GROUP INPUT INTO THE CAPITAL PROGRAMME

1 INFRASTRUCTURE STRATEGY

We began with the Steering Group on the Infrastructure Strategy Prioritisation

June - July LTP Steering Groups



2 PRIORITISATION FRAMEWORK

We then agreed the prioritisation framework.

August – September LTP Steering Groups



3 CORE PROGRAMME

Prioritisation framework applied
→ core programme + strategic candidates

29 September Steering Group

TODAY'S SESSION (29 OCT STEERING GROUP)

Bringing it together: resulting programme options, overall investment levels and trade-offs

WHAT'S NEXT: 3 NOVEMBER STEERING GROUP

Final Steering Group confirmation of capital programme following 29 October feedback

Direction sought



Provide in-principle direction on the preferred capital programme to progress, including any discrete project changes or requests, for final confirmation on 3 November.

29 OCT • IN-PRINCIPLE DIRECTION



3 NOV • FINAL CONFIRMATION

Property & Infrastructure Capital Programme Options: \$400m, \$500m and \$600m

A summary of the Property & Infrastructure CAPEX scenarios

Introduction – Infrastructure programme

Property and Infrastructure (P&I) is preparing capital expenditure information for the Long Term Plan 2027-2037 (LTP). This information covers transportation, waste minimisation and management, and the aspects of property that don't relate to the provision of Community Services (instead that is covered by the equivalent exercise led by Community Services).

As part of the LTP development process, P&I has prepared three capital programme options. These options are built to notional net expenditure levels of \$400 million, \$500 million, and \$600 million over ten years. The options are intended to inform initial financial modelling, and with that, to help elected members understand the choices and trade-offs that may be involved at different funding levels. The options summarised in this pack show what could be delivered at each level of investment, and what may need to be deferred or excluded as a result. All three options share a common core of renewals and committed projects. The higher expenditure options add projects or bring work forward, mainly within Transport.

Please note:

- This material reflects information available as at 7 October 2026 and is a live working draft that may contain errors. Initiative scopes, costs, timing, and funding assumptions are still being refined. Changes are expected as further information and feedback are received. It is expected initiatives will be added, removed, or rephased before a consolidated organisational capital expenditure programme is confirmed.
- Cost estimates are indicative and uninflated, and are at differing levels of maturity; some are based on detailed design, others are early estimates with significant uncertainty. External funding assumptions, including NZTA Waka Kotahi co-funding, have not been confirmed.
- This material does not represent a Council decision or commitment to fund or deliver any project. Final decisions will be made by Council through the Long Term Plan process, including public consultation.

Option overview

Three indicative P&I capital plan options have been prepared based on a notional net expenditure cap of \$400m, \$500m, and \$600m.

CONSTRAINED

Net council spend

\$398.2M

Gross capex **\$495.9M**

External funding **\$97.7M**

Initiatives included **108 of 156**

Peak year **FY33 \$68.7M** (\$60.4M net)

Whakatipu share **61%**

Upper Clutha share **31%**

Districtwide share **8%**

MID-POINT

Net council spend

\$500.2M

Gross capex **\$597.9M**

External funding **\$97.7M**

Initiatives included **127 of 156**

Peak year **FY33 \$73.8M** (\$65.4M net)

Whakatipu share **63%**

Upper Clutha share **31%**

Districtwide share **6%**

EXTENDED

Net council spend

\$599.8M

Gross capex **\$697.5M**

External funding **\$97.7M**

Initiatives included **137 of 156**

Peak year **FY34 \$84.6M** (\$79.2M net)

Whakatipu share **58%**

Upper Clutha share **34%**


Districtwide share **8%**

External funding is the same in all three scenarios (\$97.7M)

Only external funding with a 'high' probability of being secured is included – all related initiatives are in the 'core' programme

Annual spend comparison

■ \$398m / \$496m
 ■ \$500m / \$598m
 ■ \$600m / \$698m
 ■ External funding high probability only

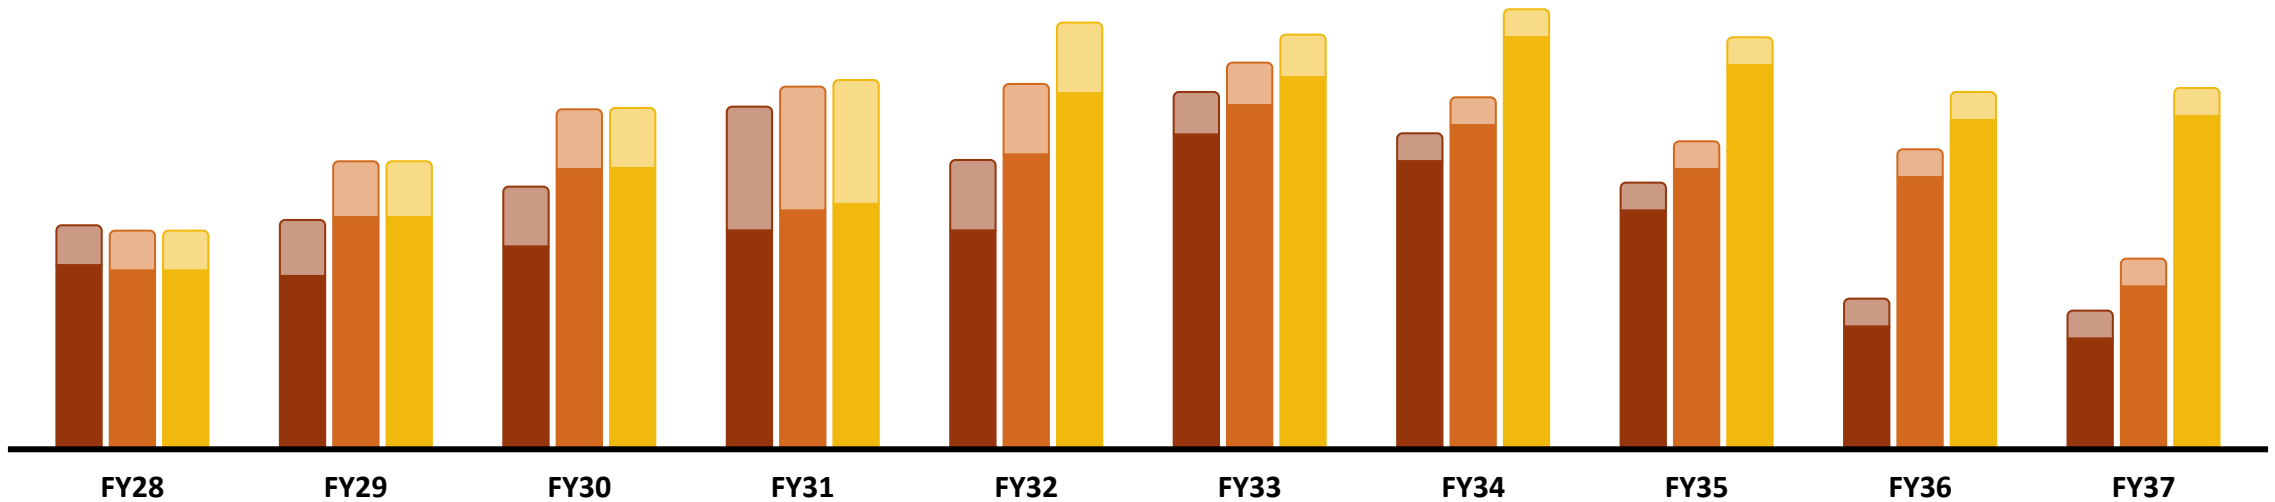


35m / 43m	33m / 44m	39m / 51m	42m / 66m	42m / 56m	60m / 69m	55m / 61m	46m / 51m	24m / 29m	21m / 27m
-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------

34m / 42m	45m / 55m	54m / 66m	46m / 70m	57m / 70m	65m / 74m	62m / 68m	54m / 59m	52m / 58m	31m / 37m
-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------

34m / 42m	45m / 55m	54m / 66m	47m / 71m	68m / 82m	71m / 79m	79m / 85m	74m / 79m	63m / 69m	64m / 70m
-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------	-----------

Major spends - all options

Eleven major initiatives are common across all scenarios. They represent 60% of spend in the lowest cost (\$400M net) option.

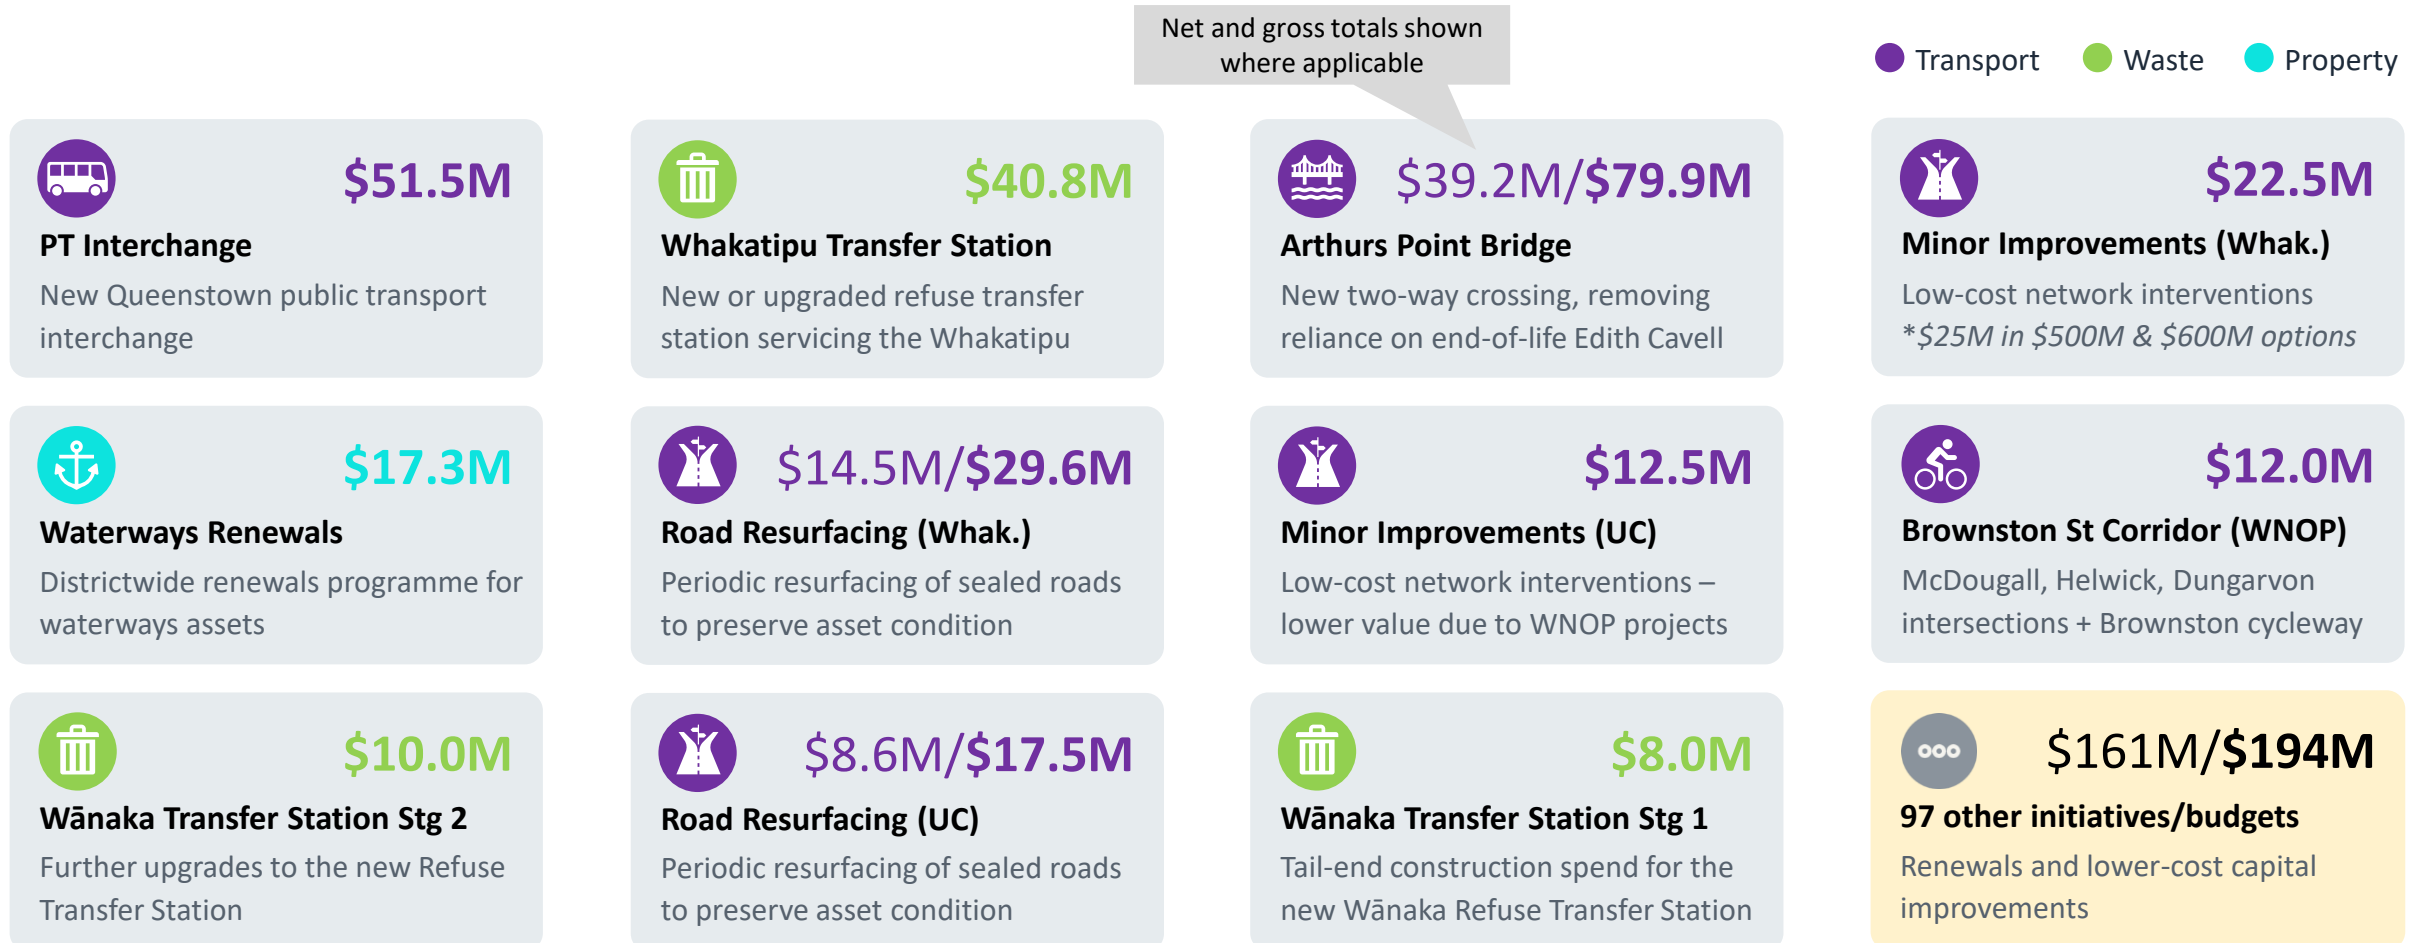

Additions - \$500M option

This option adds \$102.0M (net) spend to the lowest cost option. 23 initiatives are added or increased.

● Transport ● Property



\$29.0M

Park & Ride - Stage 1

Whakatipu Park & Ride site, most likely in the Eastern Corridor.



\$14.3M

Anderson-Aubrey-Northlake (WNOP)

Northlake & Aubrey-Gunn shared paths + Anderson Rd intersections



\$9.0M

Network Optimisations x3

Interventions to optimise transport networks in TPLM, TTSC, and Hāwea



\$7.0M

Seal Extensions (Whak.)

Sealing of high-use unsealed roads, supporting network growth



\$6.7M

Quail Rise – Hawthorne Link

Creation of a link between Quail Rise and Hawthorne Dr/SH6 roundabout



\$5.8M

Road 10 Formation

Formation of Frankton's Road 10, safely supporting increased usage



\$5.3M

West Wānaka Shared Paths (WNOP)

Shared paths: Wānaka -Mt Aspiring Stg1, West Wānaka, Orchard Rd



\$4.0M

Frankton Beach Jetty

New jetty to support future water-based public transport



\$3.7M

AT Minor Works (Whak.)

Low-cost active travel improvements across the Whakatipu basin



+\$3.5M

Seal Extensions (UC)

Sealing of high-use unsealed roads
**this option increases budget to \$7M*



+\$2.5M

Minor Improvements (Whak.)

Low cost network interventions
**option increases budget to \$25M*



\$11.1M

10 other initiatives/budgets

Investments in street lighting, CCTV expansion, and safety improvements

Additions - \$600M option

This option adds \$99.7M (net) spend to the \$500M option. 13 initiatives are added or increased.

● Transport ● Waste ● Property



\$29.0M

Park & Ride - Stage 2

Second Whakatipu Park & Ride site, most likely in the Southern Corridor.



\$26.5M

Wānaka Airport Terminal

New terminal (pending masterplan) to support increased service demand



\$13.8M

Construction Waste Facility

Districtwide processing capacity for construction & demolition waste



\$9.3M

Lower Helwick Redevelopment

Public realm improvements



+\$9.0M

Network Optimisations x3

TPLM, TTSC, and Hāwea provisions doubled to \$6M per growth area



\$5.5M

McDougall/Cardrona Valley (WNOP)

Intersection of where the McDougall shared path meets Cardrona Valley Rd



\$5.5M

Ballantyne/Sir Tim Wallis (WNOP)

Intersection safety and capacity upgrade




\$1.0M

4 other initiatives/budgets


Minor seismic works, VHF network upgrades, waste product stewardship

Spend distribution


Activity Programme-wide

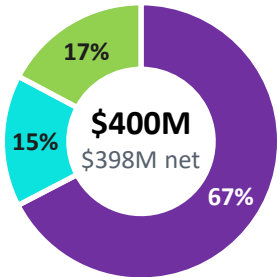

	Net	Gross
Transport	67%	73%
Property	15%	12%
Waste	17%	14%

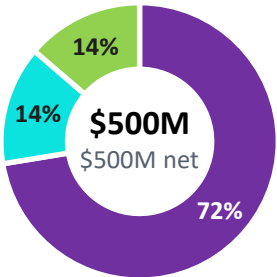


	Net	Gross
Transport	72%	77%
Property	14%	12%
Waste	14%	12%

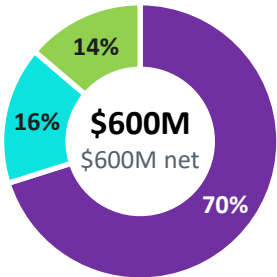


	Net	Gross
Transport	70%	74%
Property	16%	14%
Waste	14%	12%

Transport Property Waste


Cost driver Programme-wide

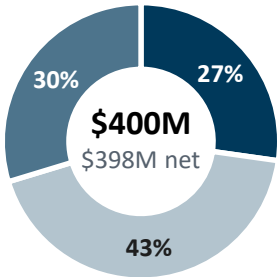

	Net	Gross
Growth	27%	24%
Renewal	43%	51%
LOS	30%	25%

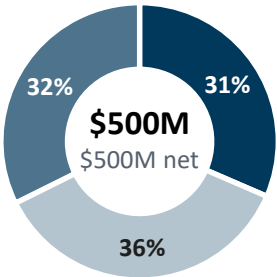

	Net	Gross
Growth	31%	28%
Renewal	36%	44%
LOS	32%	28%

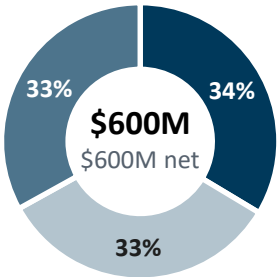


	Net	Gross
Growth	34%	31%
Renewal	33%	40%
LOS	33%	29%

Growth Renewal LOS

Consequential operating expenditure

Net opex impact builds to around \$4M per year by 2036/37. The cumulative 10-year impact is between \$25.7m - \$28.9m.

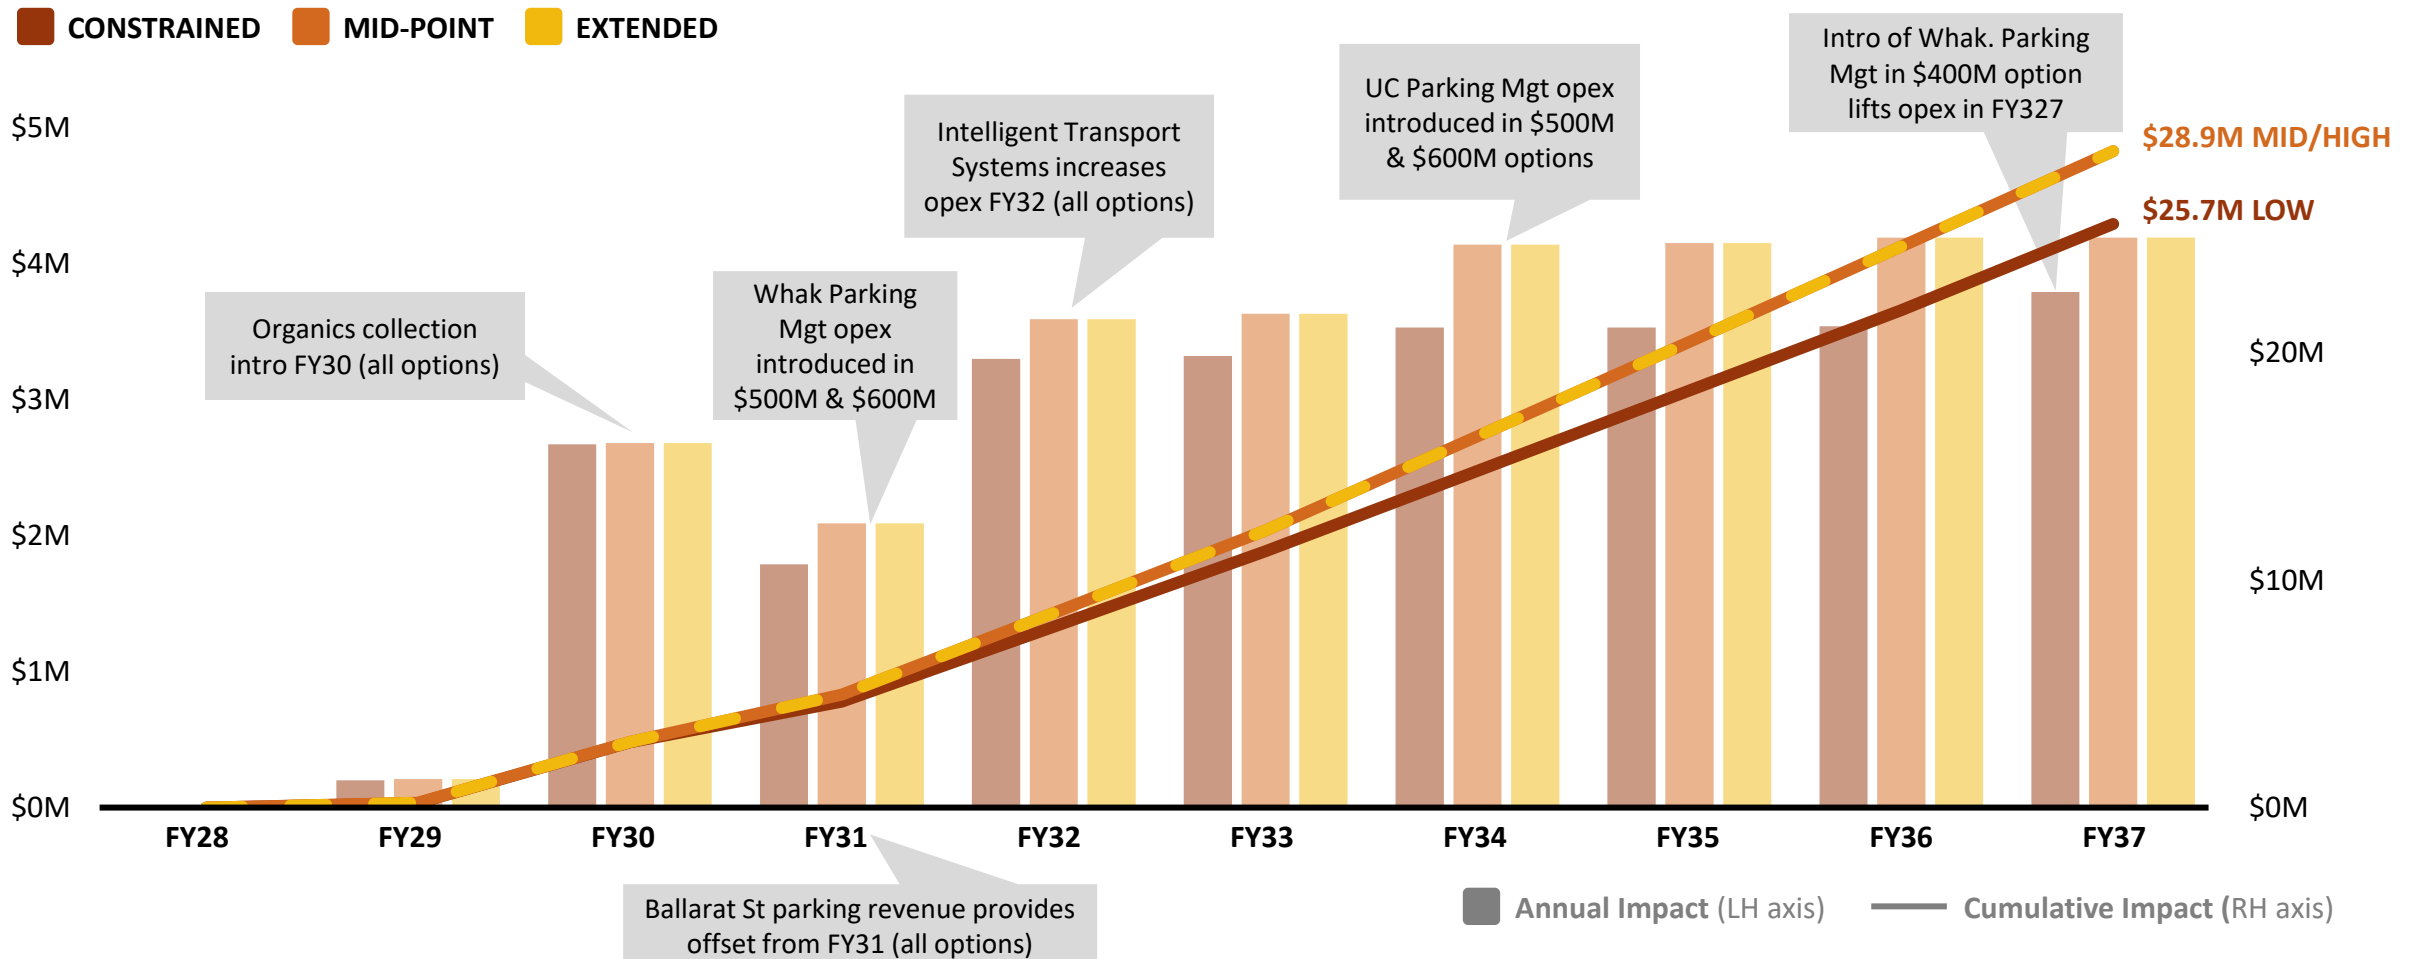

Upper Clutha – major spends, all options

Upper Clutha receives \$123.9M net at \$400M (31%). These eleven items are in every option, making up 74% of Upper Clutha's net spend.

● Transport ● Waste ● Property



\$28.8M

WNOP packages 1–5

Five Wānaka WNOP packages are in all options



\$8.6M/\$17.5M

Road Resurfacing (UC)

Periodic resurfacing of sealed roads to preserve asset condition



\$12.5M

Minor Improvements (UC)

Low-cost network interventions – lower value due to WNOP projects



\$10.0M

Wānaka Transfer Station Stg 2

Further upgrades to the new Upper Clutha Refuse Transfer Station



\$8.0M

Wānaka Transfer Station Stg 1

Tail-end construction spend for the new Wānaka Refuse Transfer Station



\$3.6M/\$7.3M

Road Metalling (UC)

Periodic renewal of unsealed road pavement layers



\$2.8M/\$5.7M

Road Rehabs (UC)

Rebuilding sealed pavements that are past economic repair



\$5.0M

Camp Hill Road Bridge

Structural upgrade or replacement to keep access resilient



\$4.9M

Airport Runway & Minor Works

Runway resurfacing, maintenance shed and minor airfield works



\$4.0M

Ardmore Street Jetty

Replacement of the jetty at the end of its useful life



\$4.0M

Vulnerable Roads (UC)

Slope, drainage and structural works to reduce closure risk



\$31.8M/\$36.0M

30 other initiatives/budgets

Renewals and lower-cost capital improvements

Upper Clutha – additions at \$500M / \$600M

Upper Clutha net spend rises to \$154.4M in the \$500M option and \$204.5M in the \$600M option (31% and 34% of each programme).

\$500M option: +\$30.5M net (8 initiatives)



\$14.3M

Anderson-Aubrey-Northlake (WNOP)

Northlake & Aubrey-Gunn shared paths + Anderson Rd intersections



\$5.3M

West Wānaka Shared Paths (WNOP)

Wānaka -Mt Aspiring Stg1, West Wānaka, Orchard Rd shared paths



+\$3.5M

Seal Extensions (UC)

Sealing of high-use unsealed roads
**this option increases budget to \$7M*



\$3.0M

Hāwea Network Optimisation

Roading improvements for Hāwea growth
**\$6.0M in the \$600M option*



\$0.75M

AT Minor Works (UC)

Low-cost active travel improvements across the Upper Clutha



\$3.6M

3 other initiatives/budgets

Wānaka office, street lighting and safety upgrades

\$600M option: +\$50.1M net (6 initiatives)



\$26.5M

Wānaka Airport Terminal

New terminal (pending masterplan) to support increased service demand



\$9.3M

Lower Helwick Redevelopment

Public realm improvements – note this may increase to ~\$20M



\$5.5M

McDougall/Cardrona Valley (WNOP)

Intersection safety and capacity upgrade



\$5.5M

Ballantyne/Sir Tim Wallis (WNOP)

Intersection safety and capacity upgrade



+\$3.0M

Hāwea Network Optimisation

Hāwea provision doubled to \$6M



\$0.2M


Seismic minor works (UC)

Assessment and any resulting minor improvements to QLDC buildings


Spend distribution – Upper Clutha

Activity


Upper Clutha
initiatives

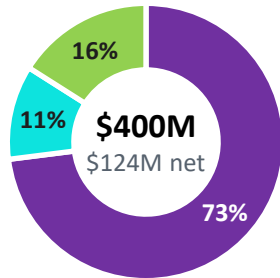

	Net	Gross
Transport	73%	77%
Property	11%	9%
Waste	16%	14%

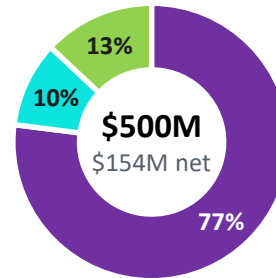

	Net	Gross
Transport	77%	79%
Property	10%	9%
Waste	13%	12%

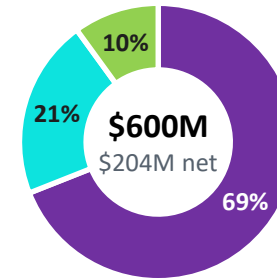


	Net	Gross
Transport	69%	72%
Property	21%	19%
Waste	10%	9%


Transport Property Waste

Cost driver


Upper Clutha
initiatives

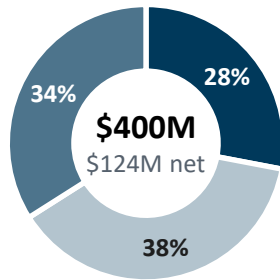

	Net	Gross
Growth	28%	24%
Renewal	38%	47%
LOS	34%	29%

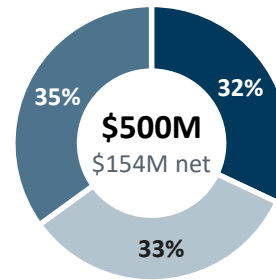

	Net	Gross
Growth	32%	29%
Renewal	33%	40%
LOS	35%	31%

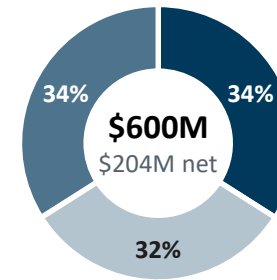

	Net	Gross
Growth	34%	31%
Renewal	32%	38%
LOS	34%	31%

Growth Renewal LOS

Whakatipu – major spends, all options

Whakatipu receives \$244.3M net at \$400M (61%). These eleven items are in every option and make up 82% of Whakatipu's share.

● Transport ● Waste ● Property



\$39.2M/\$79.9M

Arthurs Point Bridge

New two-way crossing, removing reliance on end-of-life Edith Cavell



\$51.5M

PT Interchange

New Queenstown public transport interchange



\$40.8M

Whakatipu Transfer Station

New or upgraded refuse transfer station servicing the Whakatipu



\$14.5M/\$29.6M

Road Resurfacing (Whak.)

Periodic resurfacing of sealed roads to preserve asset condition



\$22.5M

Minor Improvements (Whak.)

Low-cost network interventions
*\$25M in \$500M & \$600M options



\$7.0M/\$14.2M

Road Rehabs (Whak.)

Rebuilding sealed pavements that are past economic repair



\$5.1M/\$10.5M

Road Metalling (Whak.)

Periodic renewal of unsealed road pavement layers



\$6.5M

PT Assets (Whak.)

Stops, shelters and approaches across the Whakatipu



\$6.0M

Vulnerable Roads (Whak.)

Slope, drainage and structural works to reduce closure risk



\$5.2M

Ballarat Street Carpark

Upgrade and sealing of the gravel carpark



\$2.5M/\$5.0M

Drainage Renewals (Whak.)

Non-routine renewal of road drainage to protect pavements



\$43.5M/\$48.2M

37 other initiatives/budgets

Renewals and lower-cost capital improvements

Whakatipu – additions at \$500M / \$600M

Whakatipu net spend rises to \$314.5M in the \$500M option and \$349.8M in the \$600M option (63% and 58% of each programme).

\$500M: +\$70.2M net (13 initiatives)



\$29.0M

Park & Ride - Stage 1

Whakatipu Park & Ride site, most likely in the Eastern Corridor.



\$7.0M

Seal Extensions (Whak.)

Sealing of high-use unsealed roads, supporting network growth



\$6.7M

Quail Rise – Hawthorne Link

Creation of a link between Quail Rise and Hawthorne Dr/SH6 roundabout



\$6.0M

Network Optimisations x2

TPLM and TTSC growth areas, \$3M each



\$5.8M

Road 10 Formation

Formation of Frankton's Road 10, safely supporting increased usage



\$4.0M

Frankton Beach Jetty

New jetty to support future water-based public transport



\$3.7M

AT Minor Works (Whak.)

Low-cost active travel improvements across the Whakatipu basin



+\$2.5M

Minor Improvements (Whak.)

Low cost network interventions
**option increases budget to \$25M*



\$5.4M

4 other initiatives/budgets

PT network optimisation, Gorge Rd active travel, lighting, safety

\$600M: +\$35.3M net (4 initiatives)



\$29.0M

Park & Ride - Stage 2

Second Whakatipu Park & Ride site, most likely in the Southern Corridor.



+\$6.0M

Network Optimisations x2

TTSC & TPLM network optimisations rise from \$3M to \$6M each



\$0.3M


Seismic minor works (Whak.)

Assessment and any resulting minor improvements of QLDC buildings


Spend distribution – Whakatipu

Activity


Whakatipu initiatives

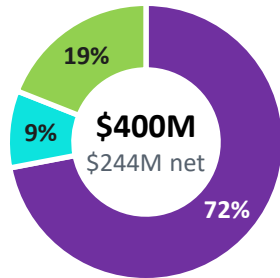

	Net	Gross
Transport	72%	79%
Property	9%	7%
Waste	19%	14%

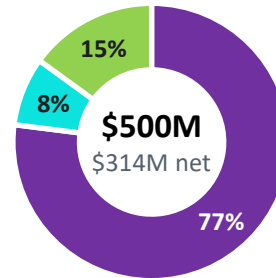

	Net	Gross
Transport	77%	81%
Property	8%	7%
Waste	15%	12%

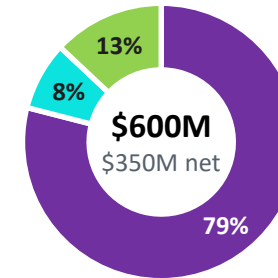


	Net	Gross
Transport	79%	83%
Property	8%	6%
Waste	13%	11%


Transport Property Waste

Cost driver


Whakatipu initiatives

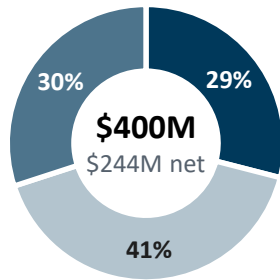

	Net	Gross
Growth	29%	25%
Renewal	41%	51%
LOS	30%	24%

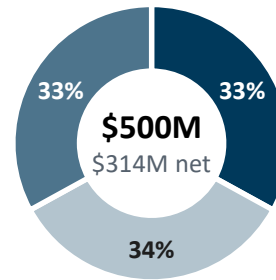

	Net	Gross
Growth	33%	29%
Renewal	34%	43%
LOS	33%	28%

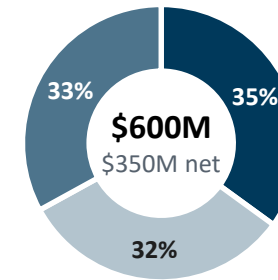

	Net	Gross
Growth	35%	32%
Renewal	32%	40%
LOS	33%	28%

Growth Renewal LOS

Districtwide – major spends and additions

Districtwide initiatives total \$30.0M net at \$400M (8%), rising to \$31.3M at \$500M and \$45.5M at \$600M.

All options: \$30.0M net (15 initiatives, \$32.2M gross)



\$17.3M

Waterways Renewals

Districtwide renewals programme for waterways assets



\$5.0M

QLDC Office Building Renewals

Planned minor renewals of QLDC office buildings



\$0.8M/\$3.0M

Organic Waste Management

Kerbside food scraps and green waste bins (75% third-party funded)



\$1.7M

QLDC Office FF&E Renewals

Lifecycle replacement of office furniture, fittings and equipment



\$1.0M

CCTV Renewals

Renewal of existing CCTV cameras and network at end of life



\$4.2M

10 other initiatives/budgets

Transport model, former landfills, heritage bldgs, parking plan, bins, AMPs

\$500M: +\$1.3M net (2 initiatives)



\$1.1M

CCTV Network Expansion

Expansion of the CCTV network, including video analytics



\$0.2M

Building Management System

System to monitor and control building services



\$13.8M

Construction Waste Facility

Districtwide processing capacity for construction & demolition waste



\$0.3M

Product Stewardship

Facilities and initiatives that enable product take-back schemes



\$0.2M

VHF Network Upgrade

Upgrade for reliable district-wide radio communications

Total spend by period

Depending on the option, Whakatipu receives 58-63% of net spend and Upper Clutha 31-34%


Whakatipu Upper Clutha Districtwide

Y1–3 FY28–FY30


Y4–6 FY31–FY33

Y7–10 FY34–FY37


\$400M



Upper Clutha 41%
\$44.0M net
Whakatipu 49%
\$53.2M net
Districtwide 10% · \$10.3M




Upper Clutha 25%
\$36.7M net
Whakatipu 69%
\$99.5M net
Districtwide 6% · \$8.5M




Upper Clutha 30%
\$43.2M net
Whakatipu 63%
\$91.6M net
Districtwide 8% · \$11.2M


\$500M



Upper Clutha 44%
\$58.4M net
Whakatipu 48%
\$63.5M net
Districtwide 8% · \$10.8M




Upper Clutha 28%
\$46.2M net
Whakatipu 67%
\$112.9M net
Districtwide 5% · \$8.8M




Upper Clutha 25%
\$49.8M net
Whakatipu 69%
\$138.0M net
Districtwide 6% · \$11.6M


\$600M



Upper Clutha 44%
\$58.4M net
Whakatipu 48%
\$63.5M net
Districtwide 8% · \$11.1M



Upper Clutha 26%
\$48.2M net
Whakatipu 62%
\$115.9M net
Districtwide 12% · \$22.3M



Upper Clutha 35%
\$97.9M net
Whakatipu 61%
\$170.4M net
Districtwide 4% · \$12.1M

Total net capital spend, all activities (\$M), by area and period; centre figure = total for the period. \$600M Districtwide rises in Y4–6 with the Construction Waste Facility.

Trade-offs between options

19 initiatives are excluded at \$400M that are included from \$500M. 10 initiatives are included only in the \$600M option.

Initiative	Activity	\$400M	\$500M	\$600M
Park & Ride Stage 1	Transport	X	\$29.0M	\$29.0M
Anderson-Aubrey-Northlake	Transport	X	\$14.3M	\$14.3M
Seal Extensions – Whakatipu	Transport	X	\$7.0M	\$7.0M
Quail Rise-Hawthorne Link	Transport	X	\$6.7M	\$6.7M
Hāwea Network Optimisation	Transport	X	\$3.0M	\$6.0M
TPLM Network Optimisation	Transport	X	\$3.0M	\$6.0M
TTSC Network Optimisation	Transport	X	\$3.0M	\$6.0M
Road 10 Formation	Transport	X	\$5.8M	\$5.8M
West Wānaka Shared Paths	Transport	X	\$5.3M	\$5.3M
Frankton Beach Jetty	Property	X	\$4.0M	\$4.0M
AT Minor Works – Whakatipu	Transport	X	\$3.7M	\$3.7M
PT Network Optimisation	Transport	X	\$2.0M	\$2.0M
Wānaka Office Improvements	Property	X	\$2.0M	\$2.0M

Initiative	Activity	\$400M	\$500M	\$600M
Gorge/Robins Rd Active Travel	Transport	X	\$1.6M	\$1.6M
CCTV Network Expansion	Property	X	\$1.1M	\$1.1M
AT Minor Works – Upper Clutha	Transport	X	\$0.75M	\$0.75M
Safety/Accessibility Upgrades	Property	X	\$1.0M	\$1.0M
Building Management System	Property	X	\$0.17M	\$0.17M
Park & Ride Stage 2	Transport	X	X	\$29.0M
Wānaka Airport New Terminal	Property	X	X	\$26.5M
Construction Waste Facility	Waste	X	X	\$13.8M
Lower Helwick Redevelopment	Transport	X	X	\$9.3M
McDougall/Cardrona Vall. Inter.	Transport	X	X	\$5.5M
Ballantyne/Sir Tim Wallis Inter.	Transport	X	X	\$5.5M
Seismic Minor Works	Property	X	X	\$0.52M
Product Stewardship	Waste	X	X	\$0.30M
VHF Network Upgrade	Property	X	X	\$0.20M

Key WUCCB priority for
Council consideration

Modelling exclusions

18 initiatives (presented to Council 19 Aug 2026) excluded from the P&I options + 10 initiatives excluded by PILT prior to long-list stage.

Initiative	Activity	Estimate	Notes
<i>TBC: Arterial Stage 2</i>	<i>Transport</i>	<i>\$85.1M</i>	<i>Not incl. in P&I options. MRF & Office pending Council decision. Revisit Arterial 2 alignment</i>
<i>TBC: Material Recovery Facility</i>	<i>Waste</i>	<i>\$71.1M</i>	
<i>TBC: New QLDC Office Building</i>	<i>Property</i>	<i>\$67.0M</i>	
Arterial Stage 3	Transport	\$150.1M	Excluded by Council on 29 Sept. 2026
Town Centre Parking Building/s	Transport	\$115.0M	
Church/Earl/Marine Pub. Realm	Transport	\$62.8M	
Memorial Centre Replacement	Property	\$58.5M	
Camp/Ballarat Public Realm	Transport	\$42.0M	
Lake Esplanade Public Realm	Transport	\$34.4M	
Skippers Road & Bridge	Transport	\$15.0M	
Time of Use Charging	Transport	\$12.0M	Lower P&I Leadership priority at this time relative to other initiatives...
Lynch Block Site Preparation	Property	\$5.4M	
Solar Energy Conversion	Property	\$4.9M	

One Mile-Sunshine Bay AT	Transport	\$4.9M	...further understanding needed and/or alternative arrangements planned or possible. Council to consider inclusion/exclusion.
Butlers Green Retaining Wall	Transport	\$1.8M	
Fernhill Active Travel Link	Transport	\$1.6M	
Wānaka CBD Pathway Surfacing	Transport	\$1.0M	
EV Charging Stations	Property	\$0.3M	
Whakatipu Mass Rapid Transit	Transport	\$800.0M	Initiatives excluded by P&I Leadership developing the P&I proposed longlist (as presented to Council workshop previously). Alternative funding and delivery mechanisms could be explored for some initiatives.
Kawarau Falls Bridge 2	Transport	\$705.5M	
Arrow Jn to Town Centre Cdr.	Transport	\$22.5M	
Northlake-Anderson Link	Transport	\$15.3M	
Park St Active Travel	Transport	\$10.0M	
Jacks Pt to Jardine Park AT	Transport	\$10.0M	
Arrowtown to Lake Hayes AT	Transport	\$10.0M	
Kelvin Pen. to Frankton AT	Transport	\$10.0M	
LHE to Frankton via K River AT	Transport	\$10.0M	
Strategic Land Acquisition	Property	\$9.3M	

Community Services Capital Programme Options: \$400m and \$500m

A summary of the Community Services CAPEX scenarios

Options overview

Two Community Services capital plan options have been prepared based on gross expenditure scenarios.

CONSTRAINED

\$448.4M

Gross capex **\$448.4M**

Projects included: **164 of 230**

Peak year FY28: **\$67.2M**

Whakatipu share: **46.7%**

Upper Clutha share: **38.6%**

MID-POINT

\$515.3M

Gross capex **\$515.3M**

Projects included **177 of 230**

Peak year FY28 **\$67.2M**

Whakatipu share **48.9%**

Upper Clutha share **37.7%**


EXTENDED

\$600.0M

This level of spend is not currently achievable from a deliverability, resourcing and scheduling perspective

Community Services gross CAPEX scenarios derived from a \$400m and \$500m programme sequencing analysis.

Annual spend comparison

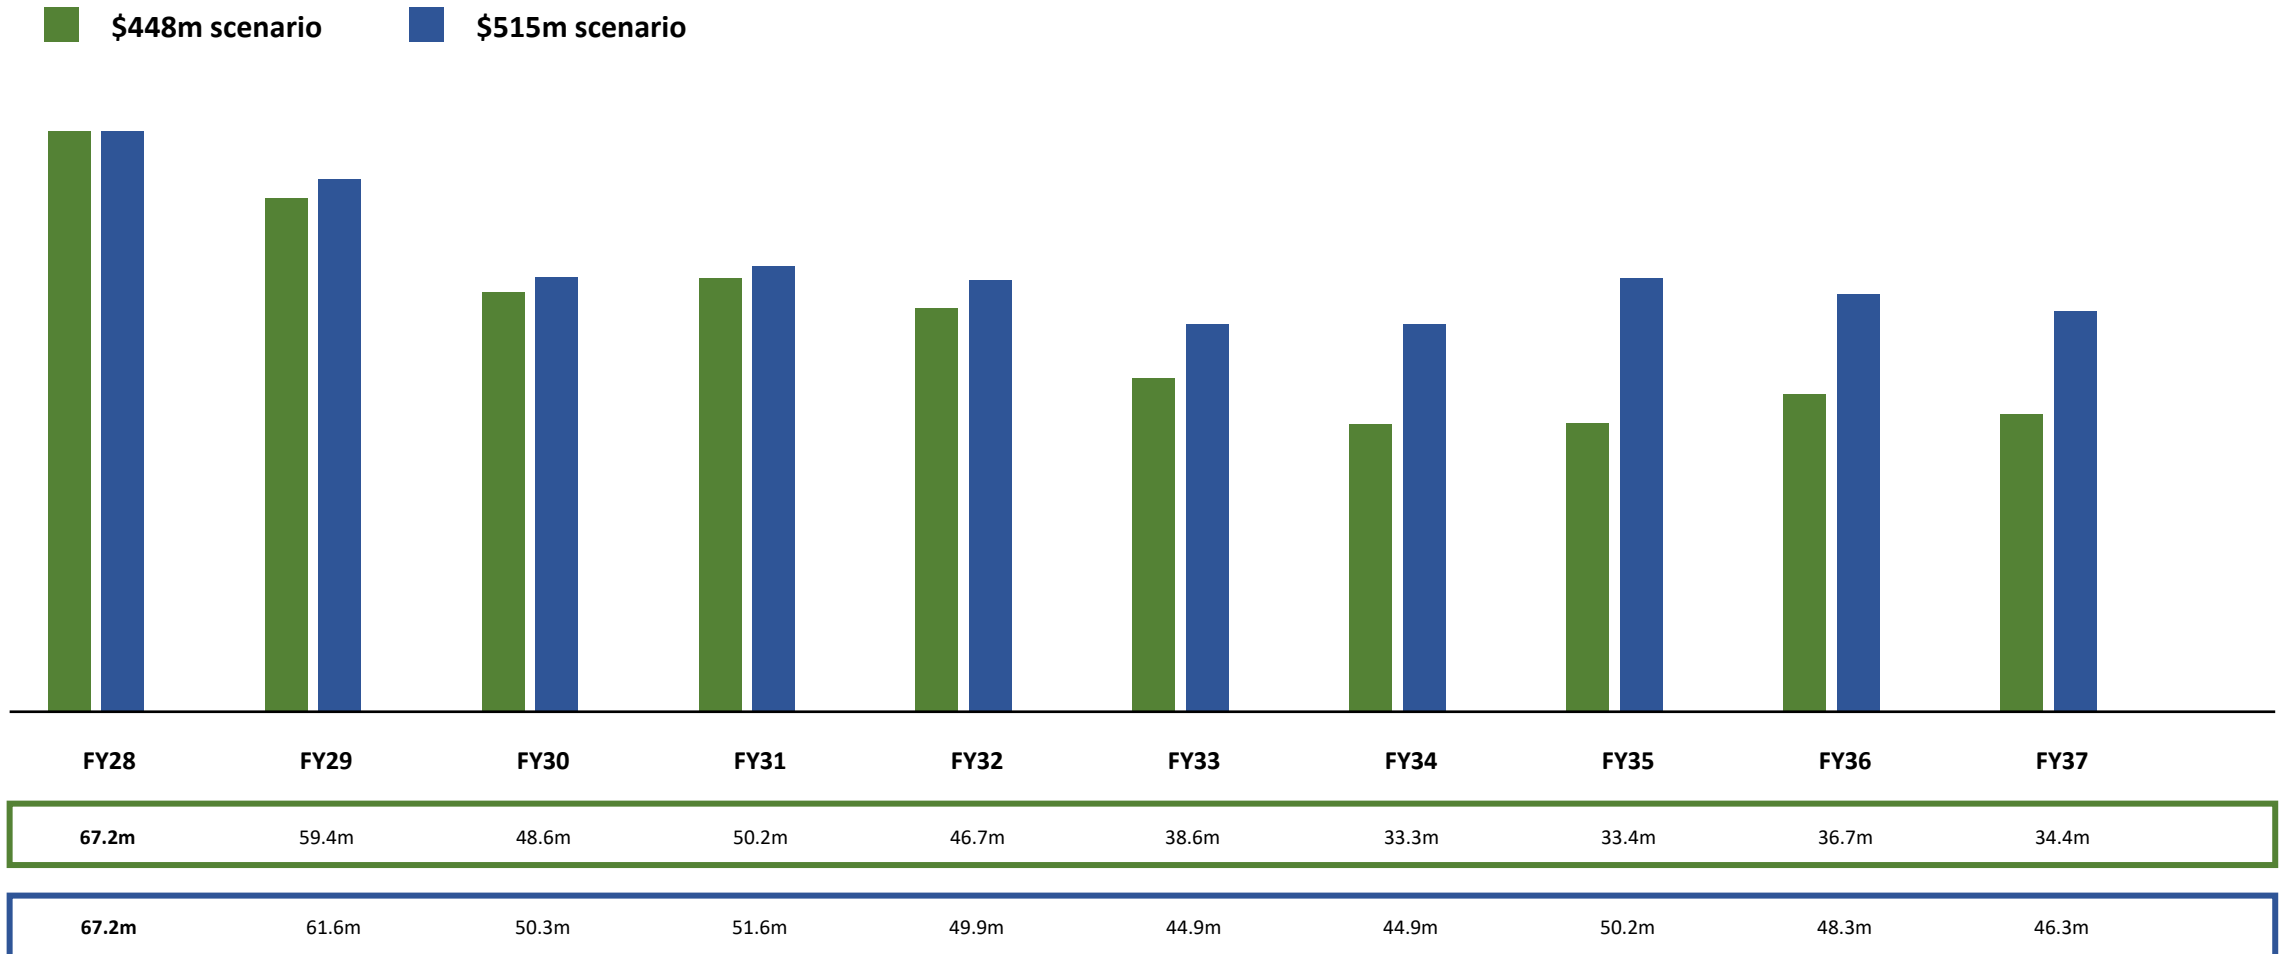

The Community Services gross expenditure scenarios based on sequencing and options analysis.
Note that additional work is required to smooth the program over the 10 years, particularly the \$448m scenario.

Whakatipu LTP 27–37 Capital Programme - \$515m Option

WHAKATIPU | HIGHER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$44.5M

QEC - New 4x Indoor Courts,
Well, Carpark



\$30.4M

Community Infrastructure
Land Purchase



\$27.0M

Ladies Mile Community
Centre



\$19.5M

Wildfire Mitigation
Programme



\$17.0M

QEC - Shared Community
Clubrooms



\$12.8M

QEC Hydroslides



\$10.1M

New Sports Fields in
Queenstown



\$8.5M

Southern Corridor
Community Centre



\$6.7M

Southern Corridor Local
Library



\$6.2M

Lakeview Development -
Plaza



\$5.9M

Glenorchy Floodbank
Programme



\$4.7M

QEC - Energy Upgrade



\$4.2M

New & Replacement Toilets -
Wakatipu



\$3.8M

Project Tohu - Coronet Forest
Revegetation



\$3.7M

Warren Park Development
Plan Actions



\$3.4M

Blue Green Network Plan -
Targeted Actions



\$3.0M

New Playgrounds -
Whakatipu



\$3.0M

New Sports Field Floodlights
- Waka



\$2.6M

Pest Animal Programme -
Wakatipu



\$2.1M

Community Services Project
Initiatives



\$2.0M

Southern Corridor Aquatic
Centre



\$1.9M

Parks Open Spaces Minor
Improvements – Wakatipu



\$1.8M

Queenstown Gardens Tree
Succession Plan

Whakatipu LTP 27–37 Capital Programme - \$515m Option

WHAKATIPU | LOWER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$1.6M

Arrowtown Reserves
Development Plan
Implementation



\$1.4M

Cemeteries Minor
Improvements - Wakatipu



\$1.3M

Parks Biodiversity
Partnerships - Wakatipu



\$1.2M

Shotover Cemetery
Development



\$1.2M

Sunshine Bay Fernhill Dev
Plan Actions



\$1.1M

Blue Green Network Plan -
Baseline Actions



\$1.1M

Lake Hayes Showground
Reserve Development



\$1.0M

QEC - Indoor Courts New
Capex (Sport)



\$915K

Ben Lomond and QT Hill RMP
Actions



\$758K

QEC Hydrolides Demolition



\$661K

Queenstown Gardens
Development



\$651K

Queenstown Marina Sugar
Lane Development



\$649K

Jardine Park Development
Plan implementation



\$623K

NPS Natural Hazard
Mitigation



\$609K

Widgeon Place Development
Plan Implementation



\$566K

QEC - Trailorise the event
portacoms x5



\$508K

Community Park Eastern
Corridor



\$508K

Community Park Southern
Corridor



\$370K

Libraries - New Mobile Van



\$350K

QEC - New gym equipment if
we get 800m2 gym extension



\$295K

Southern Corridor
Recreation Facilities



\$152K

QEC - New trailorised
grandstands x3



\$30K

Kingston Lakeside
Development Plan



\$67.5M

50 Other Initiatives/Budgets

CS renewals and lower-cost capital
improvements

Wānaka LTP 27–37 Capital Programme - \$515m Option

UPPER CLUTHA | HIGHER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$27.3M

WRC - Building Extension -
Stage)



\$24.0M

New Wānaka Library Hub
Building



\$19.4M

Ballantyne Rd Sports Hub -
Stage 2



\$16.0M

Wānaka Pool Leisure
Extension



\$14.8M

Wānaka North Community
Centre



\$8.5M

Ballantyne Rd Sports Hub -
Stage 1



\$8.5M

Wānaka Lakefront
Development Plan Stage 4



\$6.7M

New Sports Fields in Wānaka



\$4.2M

New & Replacement Toilets -
Wānaka



\$3.5M

Wānaka Artifical Turf -
Football/Rugby



\$3.0M

New Playgrounds - Wānaka



\$3.0M

New Sports Field Floodlights
- Wānaka



\$2.6M

Pest Animal Programme -
Wānaka



\$2.3M

Wānaka Pool - Energy
Upgrade

Wānaka LTP 27–37 Capital Programme - \$515m Option

UPPER CLUTHA | LOWER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$1.3M

**Parks Biodiversity
Partnerships - Wānaka**



\$1.3M

**Parks Open Spaces Minor
Improvements – Wānaka**



\$1.1M

**Cemeteries Minor
Improvements - Wānaka**



\$1.1M

**Wānaka South Community
Centre**



\$776K

**Eely Point Tree Succession
Plan**



\$660K

**Wānaka Lakefront
Development Plan Stage 6**



\$508K

Community Park Wānaka



\$508K

**Community Park Wānaka
North**



\$508K

**Community Park Wānaka
South**



\$285K

**Lismore Park Development
Plan Implementation**



\$203K

**Wānaka Lakefront
Development Plan Stg 2**



\$152K

**Wānaka A&P Showgrounds
Improvements**



\$1

**Wānaka Performing Arts
Precinct (Placeholder)**



\$39.7M

38 Other Initiatives/Budgets

CS renewals and lower-cost capital
improvements

Whakatipu LTP 27–37 Capital Programme - \$448m Option

WHAKATIPU | HIGHER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$44.5M

QEC - New 4x Indoor Courts,
Well, Carpark



\$30.5M

Community Infrastructure
Land Purchase



\$27.0M

Ladies Mile Community
Centre



\$19.6M

Wildfire Mitigation
Programme



\$12.8M

QEC Hydroslices



\$9.5M

New Sports Fields in
Queenstown



\$6.2M

Lakeview Development -
Plaza



\$5.9M

Glenorchy Floodbank
Programme



\$4.7M

QEC - Energy Upgrade



\$4.2M

New & Replacement Toilets -
Wakatipu



\$3.8M

Project Tohu - Coronet Forest
Revegetation



\$3.1M

New Sports Field Floodlights
- Waka



\$3.1M

New Playgrounds -
Whakatipu



\$2.6M

Pest Animal Programme -
Wakatipu



\$2.1M

Community Services Project
Initiatives



\$2.0M

Southern Corridor Aquatic
Centre



\$1.9M

Parks Open Spaces Minor
Improvements – Wakatipu



\$1.8M

Queenstown Gardens Tree
Succession Plan

Whakatipu LTP 27–37 Capital Programme - \$448m Option

WHAKATIPU | LOWER-VALUE PROJECTS

Projects are ordered by expenditure. Colours indicate programme.

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$1.4M

Cemeteries Minor
Improvements - Wakatipu



\$1.3M

Parks Biodiversity
Partnerships - Wakatipu



\$1.2M

Shotover Cemetery
Development



\$1.1M

Blue Green Network Plan -
Baseline Actions



\$1.0M

QEC - Indoor Courts New
Capex (Sport)



\$758K

QEC Hydroslides Demolition



\$623K

NPS Natural Hazard
Mitigation



\$597K

Southern Corridor
Community Centre



\$566K

QEC - Trailorise the event
portacoms x5



\$512K

Community Park Southern
Corridor



\$510K

Community Park Eastern
Corridor



\$466K

Southern Corridor Local
Library



\$371K

Libraries - New Mobile Van



\$350K

QEC - New gym equipment if
we get 800m2 gym extension



\$296K

Southern Corridor
Recreation Facilities



\$30K

Kingston Lakeside
Development Plan



\$81M

65 Other Initiatives
Budgets
CS Renewals and lower cost
capital improvements

Wānaka LTP 27–37 Capital Programme - \$448m Option

UPPER CLUTHA | HIGHER-VALUE PROJECTS

Projects ordered from highest to lowest expenditure

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$27.5M

WRC - Building Extension
Stage 1



\$24.0M

New Wānaka Library Hub
Building



\$16.1M

Wānaka Pool Leisure
Extension



\$14.9M

Wānaka North Community
Centre



\$8.5M

Ballantyne Rd Sports Hub
Stage 1



\$8.5M

Wānaka Lakefront
Development Plan Stg 4



\$6.4M

New Sports Fields in Wānaka



\$4.2M

New & Replacement Toilets -
Wānaka



\$3.5M

Wānaka Artificial Turf -
Football/Rugby



\$3.1M

New Playgrounds - Wānaka



\$2.6M

Pest Animal Programme -
Wānaka



\$2.3M

Wānaka Pool - Energy
Upgrade



\$2.3M

New Sports Field Floodlights
- Wānaka

Wānaka LTP 27–37 Capital Programme - \$448m Option

UPPER CLUTHA | LOWER-VALUE PROJECTS

Projects ordered from highest to lowest expenditure

● Venues and Facilities

● Parks and Reserves

● Libraries

● Other Initiatives



\$1.3M

**Parks Biodiversity
Partnerships - Wānaka**



\$1.3M

**Parks Open Spaces Minor
Improvements – Wānaka**



\$1.1M

**Cemeteries Minor
Improvements - Wānaka**



\$1.1M

**Wānaka South Community
Centre**



\$778K

**Eely Point Tree Succession
Plan**



\$511K

**Community Park Wānaka
South**



\$510K

Community Park Wānaka



\$508K

**Community Park Wānaka
North**



\$204K

**Wānaka Lakefront
Development Plan Stg 2**



\$152K

**Wānaka A&P Showgrounds
Improvements**



\$1

**Wānaka Arts Precinct
(Placeholder)**



\$1

**Hāwea Library - Hours
Extension**



\$32.8M

**25
Other Initiatives/Budgets**

CS Renewals and lower cost
capital improvements

Risks, Deliverability & Alignment

Six factors to actively manage across planning, governance and delivery

Business Continuity

Deferred renewals can weaken operations and maintenance of community assets. Clear AMP priorities, preventative and reactive maintenance plans, and regular reporting will protect service continuity.

Community Wellbeing

Reprioritisation or delays may lower satisfaction, social cohesion, community health and wellbeing, and Council reputation. Use clear programme timelines and delivery methods to maintain momentum and capital spend.

Infrastructure Constraints

Growth, land availability and the timing of 3 Waters infrastructure may delay community facilities. Maintaining close coordination with Alpine Waters to clarify staging and alignment will be required.

Market Constraints

Inconsistent annual spend and limited market capacity may compromise delivery. Improve pipeline visibility, work consistently with planning and delivery providers, understand constraints, and bundle work where practical.

Affordability

The proposed plan contains significant increases in capital and consequential operating costs. Embed value for money in design, construction and governance, and pursue third-party investment to reduce the impact on Council.

Deliverability Capability

A larger programme requires stronger governance, sufficient staffing and fit-for-purpose delivery methods. Review capability early and plan for increased Council operating expenditure in the first three years.


Community Services Activity Spend Distribution

 Venues & Facilities  Parks & Reserves  Libraries

All Community Services


Programme-wide

All CS 448M



	Gross
Libraries	7.5%
Parks & Reserves	45.6%
Venues & Facilities	46.9%

All CS 515M




	Gross
Libraries	7.7%
Parks & Reserves	42.9%
Venues & Facilities	49.4%

Upper Clutha


Upper Clutha initiatives

Upper Clutha 448M



	Gross
Libraries	14.3%
Parks & Reserves	39.3%
Venues & Facilities	45.9%

Upper Clutha 515M




	Gross
Libraries	12.7%
Parks & Reserves	33.6%
Venues & Facilities	50.7%

Whakatipu


Whakatipu initiatives

Whakatipu 448M



	Gross
Libraries	1.0%
Parks & Reserves	38.8%
Venues & Facilities	60.1%

Whakatipu 515M




	Gross
Libraries	3.3%
Parks & Reserves	36.9%
Venues & Facilities	59.9%

District Wide


Initiatives across both wards

District Wide 448M



	Gross
Libraries	10.5%
Parks & Reserves	82.0%
Venues & Facilities	7.5%

District Wide 515M



	Gross
Libraries	9.9%
Parks & Reserves	83.0%
Venues & Facilities	7.1%


Community Services - Cost Drivers

Cost driver split by ward. Note that as spending increases, more major projects are completed in response to the growth and therefore the growth component increases.

Growth **Renewal** **LOS**

All CS


Programme-wide

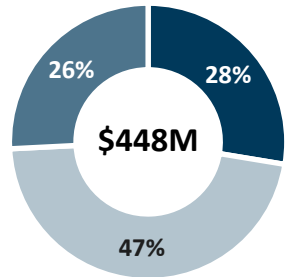

	Gross
Growth	27.6%
Renewal	46.6%
LOS	25.8%

Upper Clutha


Upper Clutha initiatives

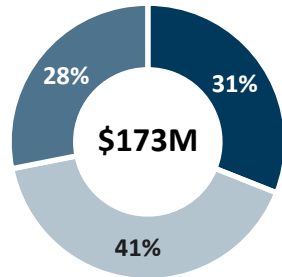

	Gross
Growth	31.0%
Renewal	40.9%
LOS	28.1%

Whakatipu


Whakatipu initiatives

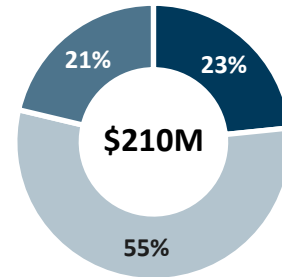


	Gross
Growth	23.4%
Renewal	55.4%
LOS	21.3%

District Wide


District-wide initiatives

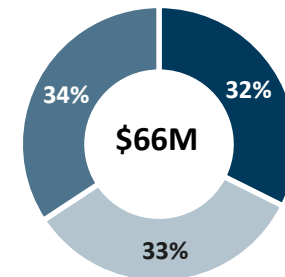


	Gross
Growth	32.4%
Renewal	33.4%
LOS	34.3%

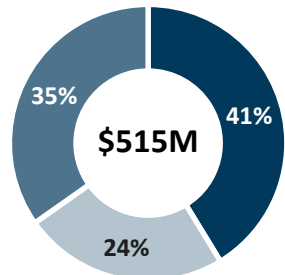


	Gross
Growth	41.3%
Renewal	24.0%
LOS	34.8%

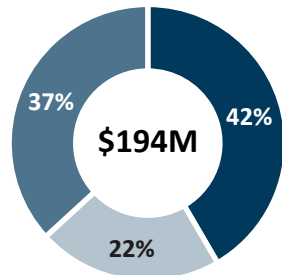

	Gross
Growth	41.6%
Renewal	21.6%
LOS	36.8%

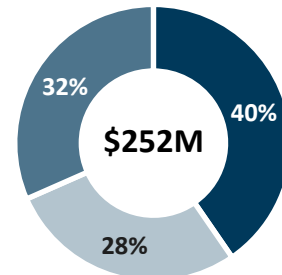

	Gross
Growth	40.4%
Renewal	28.0%
LOS	31.6%

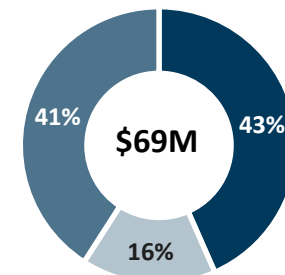

	Gross
Growth	43.4%
Renewal	15.7%
LOS	40.9%

Total spend by period – as drafted

Spend in years 1-3 is primarily in Whakatipu due to the QEC Indoor Court expansion, Aquatic Energy upgrades and Hydroslide renewal, although spend in Wānaka is higher in years 4-10.


Whakatipu Upper Clutha District wide

Y1–3 FY28–FY30


Y4–6 FY31–FY33

Y7–10 FY34–FY37


\$448M



Upper Clutha 19.5%
\$34.0M
Whakatipu 63.9%
\$111.9M
District-wide 16.7%
\$29.2M




Upper Clutha 50.7%
\$68.7M
Whakatipu 40.9%
\$55.5M
District-wide 8.4%
\$11.4M




Upper Clutha 51.2%
\$70.5M
Whakatipu 30.7%
\$42.3M
District-wide 18.2%
\$25.0M


\$515M



Upper Clutha 19.6%
\$35.0M
Whakatipu 64.2%
\$114.9M
District-wide 16.3%
\$29.2M




Upper Clutha 49.5%
\$72.5M
Whakatipu 42.0%
\$61.5M
District-wide 8.5%
\$12.5M



Upper Clutha 45.7%
\$86.7M
Whakatipu 40.0%
\$75.9M
District-wide 14.3%
\$27.2M

Net Consequential Operating Expenditure

Consequential OPEX builds to just under \$3M per year by 2036/37.

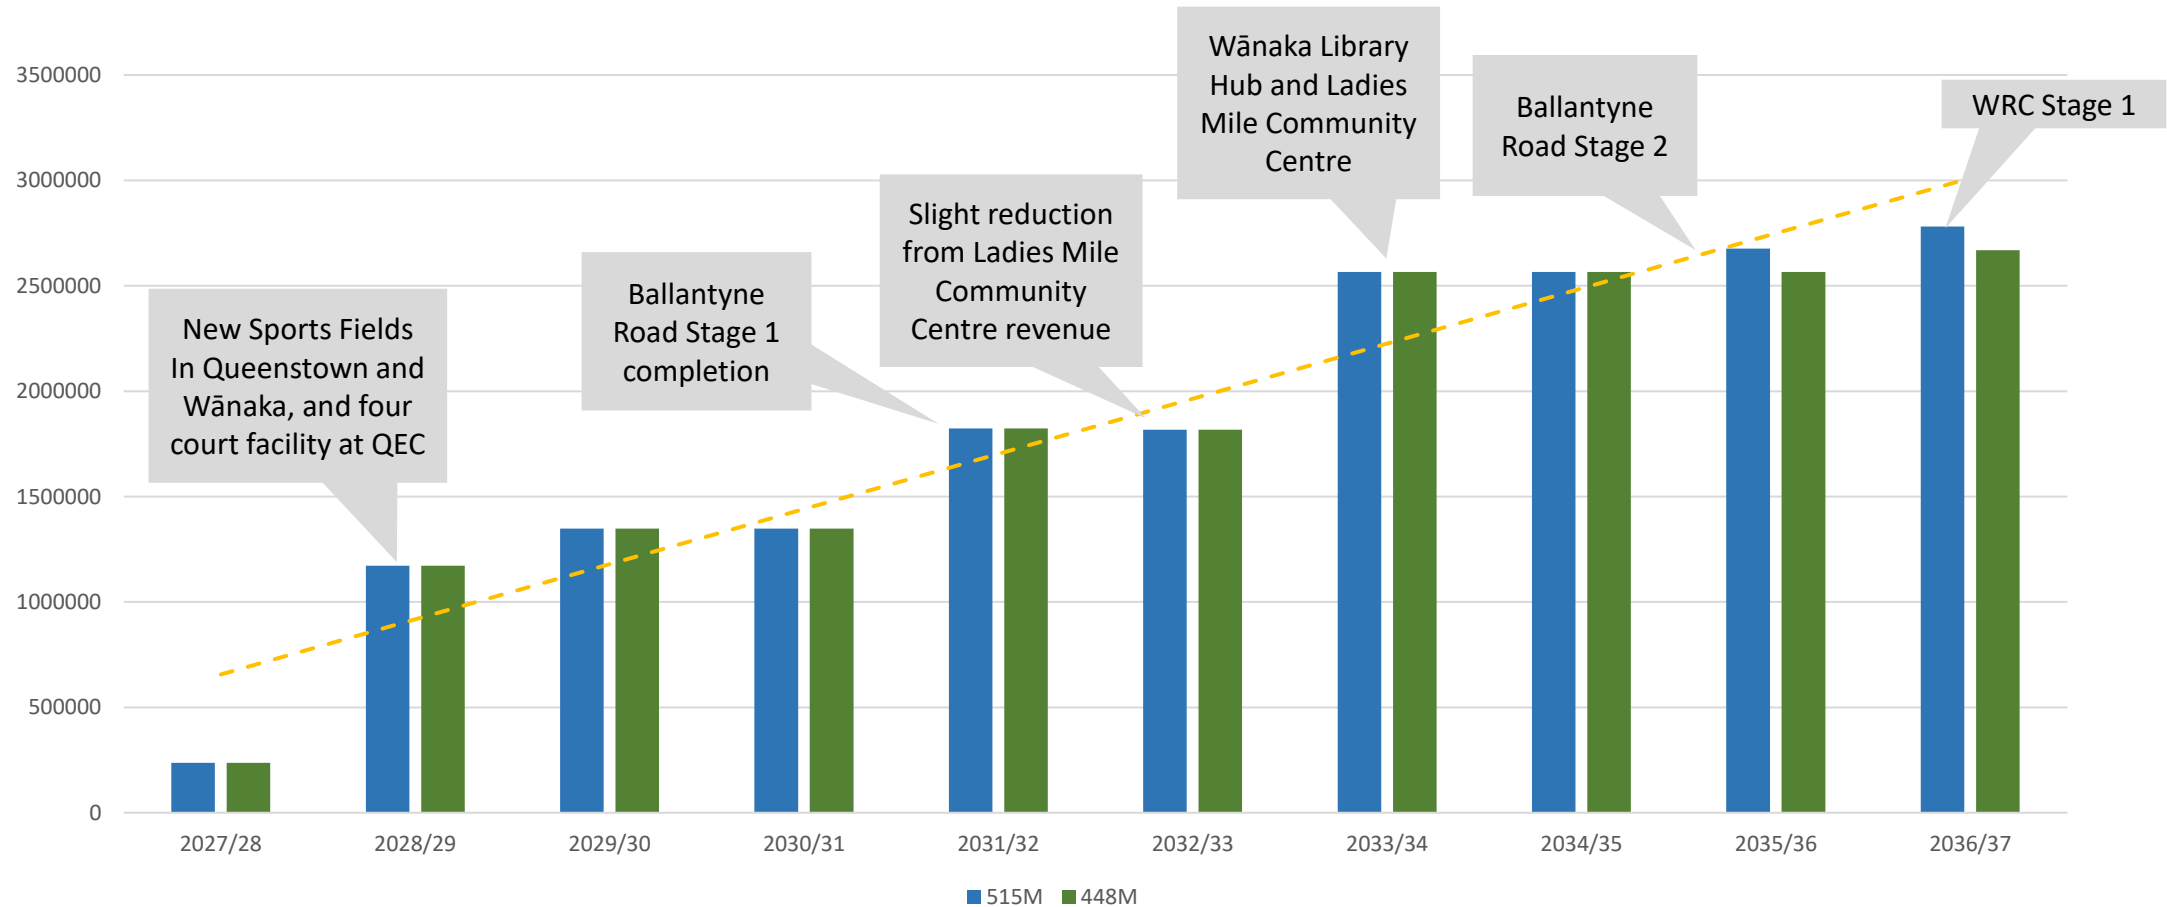

	2027/28	2028/29	2029/30	2030/31	2031/32	2032/33	2033/34	2034/35	2035/36	2036/37
\$515m	\$236,529	\$1,171,503	\$1,348,822	\$1,348,822	\$1,822,522	\$1,816,417	\$2,565,390	\$2,565,390	\$2,676,690	\$2,780,740
\$448m	\$236,529	\$1,171,503	\$1,348,822	\$1,348,822	\$1,822,522	\$1,816,417	\$2,565,390	\$2,565,390	\$2,565,390	\$2,669,440

Trade-offs Between Options

52 initiatives are excluded at \$515M, these project have been pushed to Year 11+.

Projects in blue were removed following Council direction on the 29th of September
Projects in yellow were removed following direction to change the arterial route.

Exclusions at \$515m	Department	Est Project Value
Ballantyne Rd Sports Hub - Stage 3	Parks & Reserves	\$71,645,181
Paetara - New build facility	Venues and Facilities	\$35,000,000
Wānaka Central Community Centre	Venues and Facilities	\$26,600,000
New Hawea Community Centre	Venues and Facilities	\$26,600,000
Te Atamira new build	Venues and Facilities	\$25,000,000
Frankton Library Hub - New Building	Venues and Facilities	\$17,000,000
WRC - Wellness Building extension	Venues and Facilities	\$12,610,000
QEC - New Parks Storage Complex	Venues and Facilities	\$11,297,000
Kingston Community Building - Replacement	Venues and Facilities	\$6,500,000
Queenstown Squash Replacement Building	Venues and Facilities	\$6,500,000
Glenorchy Community Building - Replacement	Venues and Facilities	\$5,745,000
Lake Hayes Pavilion - Replacement	Venues and Facilities	\$5,614,631
WRC - Outdoor Facilities	Venues and Facilities	\$5,236,500
Frankton Golf Centre - New Building	Venues and Facilities	\$5,000,000
QEC - New Carpark/Access - Grant Road	Venues and Facilities	\$4,990,000
Upper Lakes Catchment Restoration Programme	Parks & Reserves	\$4,851,230
QEC - General external works	Venues and Facilities	\$4,500,000
Hawea Community Building - Replacement	Venues and Facilities	\$4,445,000
WRC - New hockey Turf & lighting	Venues and Facilities	\$4,000,000
New District wide Hardcourts	Parks & Reserves	\$3,048,000
District-wide - Athletics Track/Facilities	Venues and Facilities	\$2,500,000
Whakatipu Rugby Club Replacement Building	Venues and Facilities	\$2,500,000
QEC - Grant Rd Sportsfields development	Venues and Facilities	\$2,288,000
Southern Corridor Aquatic Centre - Plant & Equipment Renewals	Venues and Facilities	\$2,250,000
WRC - New storage garage	Venues and Facilities	\$2,160,000
Kingston Library Extension	Libraries	\$2,000,000

Exclusions at \$515m	Department	Est Project Value
Glenorchy Library Extension	Libraries	\$1,500,000
Hawea Library Extension	Libraries	\$1,500,000
QEC - Acoustic doors- Meeting spaces	Venues and Facilities	\$1,400,000
Wānaka Central Community Centre - Building Renewals	Venues and Facilities	\$1,400,000
QEC - Foyer/cafe kiosk FF&E renewals	Venues and Facilities	\$1,192,351
QEC - Grant Road Toilet/change block	Venues and Facilities	\$1,100,000
Wānaka South Community Centre - Building Renewals	Venues and Facilities	\$1,000,000
WRC - Outdoor play area	Venues and Facilities	\$810,000
New Hawea Community Centre - Building Renewals	Venues and Facilities	\$700,000
Wānaka Central Community Centre - FF&E Renewals	Venues and Facilities	\$650,000
AI software & hardware – Aquatics drowning prevention system	Venues and Facilities	\$630,000
WRC - Pickleball & basketball outside courts	Venues and Facilities	\$620,000
QEC - Signage Renewals	Venues and Facilities	\$600,000
Paetara Signage Renewals	Venues and Facilities	\$596,176
Arrowtown Library Extension	Libraries	\$575,000
Southern Corridor Recreation Facilities - FF&E Renewals	Venues and Facilities	\$575,000
Southern Corridor Community Centre - FF&E Renewals	Venues and Facilities	\$550,000
QEC - Replace Outdoor Grandstand Seating	Venues and Facilities	\$500,000
Wānaka South Community Centre - FF&E Renewals	Venues and Facilities	\$500,000
Arrowtown Memorial Pool - Splash Pad	Venues and Facilities	\$480,000
QEC - Temporary fencing	Venues and Facilities	\$400,000
WRC - Signage renewals	Venues and Facilities	\$400,000
New Hawea Community Centre - FF&E Renewals	Venues and Facilities	\$350,000
QEC - Install permanent broadcast towers on Oval (dependant on cricket)	Venues and Facilities	\$300,000
QEC - New Sauna at Alpine Aqualand	Venues and Facilities	\$150,000
Southern Corridor Local Library - FF&E Renewals	Libraries	\$50,000

Trade-offs Between Options

An additional 15 projects excluded to achieve a \$448m programme

Projects in blue are Strategic Candidates opted for on the 29th of September, which we are suggesting for removal to achieve this budget threshold.

Note that to reduce this budget closer to \$400m, the Community Services team would need to look at reductions in current service levels, scaling back the scope of projects, or the removal of additional Strategic Candidates opted for on the 29th of September.

Additional Exclusions at \$448m	Dollar Value	Department
Ballantyne Rd Sports Hub - Stage 2	\$19,100,424	Parks & Reserves
QEC - Shared Community Clubrooms	\$16,700,000	Venues and Facilities
Warren Park Development Plan Actions	\$3,644,200	Parks & Reserves
Blue Green Network Plan - Targeted Actions	\$3,382,603	Parks & Reserves
Arrowtown Reserves Development Plan Implementation	\$1,623,000	Parks & Reserves
Sunshine Bay Fernhill Dev Plan Actions	\$1,180,000	Parks & Reserves
Lake Hayes Showground Reserve Development	\$1,060,000	Parks & Reserves
Ben Lomond and QT Hill RMP Actions	\$900,000	Parks & Reserves
Queenstown Gardens Development	\$650,000	Parks & Reserves
Wānaka Lakefront Development Plan Stage 6	\$650,000	Parks & Reserves
Jardine Park Development Plan implementation	\$640,000	Parks & Reserves
Queenstown Marina Sugar Lane Development	\$640,000	Parks & Reserves
Widgeon Place Development Plan Implementation	\$600,000	Parks & Reserves
Lismore Park Development Plan Implementation	\$280,000	Parks & Reserves
QEC - New trailorised grandstands x3	\$150,000	Venues and Facilities

Officer recommended capital programme

Community Services Capital Programme

CONSTRAINED

Net council spend

\$448.4M

Gross capex **\$448.4M**

Projects included: **164 of 230**

Peak year FY28: **\$67.2M**

Whakatipu share: **46.7%**

Upper Clutha share: **38.6%**



Property & Infrastructure Capital Programme

MID-POINT

Net council spend

\$500.2M

Gross capex **\$597.9M**

External funding **\$97.7M**

Initiatives included **127 of 156**

Peak year **FY33 \$73.8M** (\$65.4M net)

Whakatipu share **63%**

Upper Clutha share **31%**

Districtwide share **6%**

Officers recommend a capital programme of \$948.6M. We have discussed a \$1B capital programme as being an appropriate scale throughout this process.

This programme balances our district's capital investment needs with:

1. Fiscal restraint and maintaining affordability and a manageable debt profile.
2. Our assessment of what is realistically deliverable by our organisation and the market.

Adding any additional projects to the programme, if not balanced by removing equivalent cost projects from the programme, will worsen the rates increases, affordability and debt created by the programme.

Confirm directions



- Confirm Councillor in principle directions on capital programme options to proceed with
- Confirm Councillor directions for discrete project inclusions / exclusions
- We will revisit & solidify these in principle directions after seeing full financial analysis on 3 Nov

29 OCT • IN-PRINCIPLE DIRECTION



3 NOV • FINAL DIRECTION

Alternative funding: Indicative Case Studies

Alternative funding

Material TBC

Activity management plans and performance measures

Activity management plans

Activity plans: progress and open items

- The content from the Activity Plan A3s, workshopped with Councillors April-June 2026, have been integrated into the LTP Section 2 format. This is included at attachment B.
- Directions from Councillors in the Activity Plan A3 sessions have been addressed by officers.
- Proposed Levels of Service (LoS) and Key Performance Indicators (KPIs) are also presented in Section 2, pending your feedback.

Meanwhile, in Wellington...

- The Systems Improvements Act has been enacted, giving the Ministry for Cities, Environment, Regions and Transport (MCERT) the power to mandate compulsory activity structures for all NZ Councils.
- MCERT has enacted the regulations. However, they haven't yet shared the detail of what the new compulsory activity structure is! Most recent advice from Taituarā (12/10) indicated that *"it should be released in the next week or so"*.
- We will need to restructure the activity management plans to match the new compulsory structure. This work should occur over the coming fortnight, assuming we do receive the detail.

Groups of activities

Adaptation and emergency management
Community and recreational facilities
Governance, planning, and reporting
Parks and reserves
Public regulatory services
Roading and transport
Waste management and minimisation
Other

The MCERT regulations disclose the above Activity Groups, but not the crucial detail below that.

Levels of Service (LoS) and Key Performance Indicators (KPIs)

Quick facts

What was in LTP 24-34?	What is proposed for LTP 27-37?
21 distinct LoS and 55 distinct KPIs for QLDC	42 distinct LoS and 71 distinct KPIs for QLDC, more transparently and accurately reflecting our services
6 distinct LoS, 8 distinct KPIs across Sports, Recreation & Community Facilities, Parks & Reserves, Libraries	8 distinct LoS, 9 distinct KPIs across Sports, Recreation & Community Facilities, Parks & Reserves, Libraries
2 distinct LoS, 12 distinct KPIs across Transport, Property and Waste Management (excl. three waters)	14 distinct LoS, 20 distinct KPIs across Transport, Property and Waste Management (excl. three waters)

The journey

- You last saw the proposed LoS and KPIs in the Activity Plan A3s workshopped in April-June.
- Since then, they have been reviewed through senior management and refined.
- They are now provided for your review and direction.
- The next major step after your review is audit of LoS and KPIs starting 18 January.

Direction required

- Indicate if you are comfortable with the proposed LoS and KPIs as included in the Activity Management Plans at Attachment B and in more detail at Attachment C.
- Provide any feedback on anything you think should be changed or request further information.

New KPIs

Things to note:

- The KPIs on this slide and the next have been proposed as new measures.
- They aim to improve transparency by giving insight into the performance of a wider variety of Council activity areas.

Activity Plan	New KPIs	Year 1	Year 2	Year 3
Community Partnerships	Community organisations satisfied with Council support and partnerships	>85% satisfied	>85% satisfied	>90% satisfied
Libraries	Total number of physical library visits	Establish baseline	Establish baseline	Establish baseline
Libraries	Percentage of residents who are satisfied with the libraries	>80% satisfied	>80% satisfied	>80% satisfied
Transport	Percentage of town centre streets achieving a Healthy Streets Assessment score of 80% or greater.	>40%	>50%	>60%
Transport	The number of unplanned road closures (with no (or limited) detour) and the number of vehicles affected by those closures annually.	Under development	Under development	Under development
Waste Management	Compliance with resource consents for discharge to air, land, or water from waste management facilities, measured by the number of: a) abatement notices b) infringement notices c) enforcement orders d) successful prosecutions Target being no consents with any of the above noted enforcement actions (Total # of Resource Consents without an associated Enforcement Action / Total Number of Consents)	100%	100%	100%
Property	Percentage of buildings with BWOFF	100%	100%	100%
Property	Average abv building catagory A condition rating 2.5 target	80%	80%	80%
Property	Percentage of planned preventative maintenance completed annually	100%	100%	100%
Property	Percentage of renewals expenditure relative to agreed annual budget	>75%	>75%	>75%
Planning Policy	Percentage of private plan changes processed within statutory timeframes	100%	100%	100%
Building Services	Percentage of building inspections completed within 3 working days of being requested	>80%	>80%	>80%
Building Services	Percentage of Land Information Memorandum (LIM) applications processed within the statutory 10 working day timeframe	100%	100%	100%

New KPIs

Things to note:

- The KPIs on this slide have been proposed as new measures.
- They aim to improve transparency by giving more insight into performance of Council departments that previously were not measured.

Activity Plan	New KPIs	Year 1	Year 2	Year 3
Assurance, Finance, Risk	Percentage of legislatively required and high-risk Council policies reviewed by their due date.	70%	80%	90%
Emergency Management	Percentage of core EOC functional roles with sufficient trained personnel available to staff the EOC roster	100%	100%	100%
Resilience and Climate Action	Percentage of annual QLDC commitments within priority catchment and biodiversity partnership programmes that are completed to an agreed milestone or formally rephased through approved governance	90% (3yr rolling average)	90% (3yr rolling average)	90% (3yr rolling average)
Resilience and Climate Action	Hectares of Council land under active ecological restoration.	Year on year improvement	Year on year improvement	Year on year improvement
Resilience and Climate Action	Hectares of Council land under active predator or pest plant control programmes.	Year on year improvement	Year on year improvement	Year on year improvement
Corporate Services	LTPs, Annual Plans and Annual Reports are delivered within statutory timeframes and with unmodified audit opinions where relevant	100%	100%	100%
Corporate Services	% of Projects consistently meeting standards – Y1+2 (Status Reporting, Forecasting, Milestone management); - Y3 (Status Reporting, Forecasting, Milestone management, Risk & Issues management)	80%	90%	90%
Corporate Services	% of interactions with Council using digital platforms (Online payments, Online applications (e.g. Resource and Building Consents, Dogs, Change of address etc.))	Establish baseline	2% year-on-year increase	2% year-on-year increase
Corporate Services	Availability (uptime) of critical business systems and infrastructure	≥99.5%	≥99.5%	≥99.5%

Compulsory KPIs

These KPIs are required by the Department of Internal Affairs.

Activity Plan	Compulsory KPIs	Year 1	Year 2	Year 3
Transport	The change from the previous financial year in the number of fatalities and serious injury crashes on the local road network expressed as a number.	To report a decrease on the prior year	To report a decrease on the prior year	To report a decrease on the prior year
Transport	Percentage of sealed network that is resurfaced annually	5-10%	5-10%	5-10%
Transport	Average quality of ride on a sealed local road network, as measured by the Smooth Travel Exposure Index	>90%	>90%	>90%
Transport	Percentage of local footpath network that is part of the local road network that falls within the Level of Service (LOS) or service standards for the condition of footpaths.	>95%	>95%	>95%
Transport	Percentage of external contractor and internal RFS resolved within specified timeframe - Roading	95%	95%	95%

These KPIs have been directly related to the CE KPIs in the past.

Activity Plan	Related to CE KPIs	Year 1	Year 2	Year 3
Sport, Recreation and Community Venues	Percentage of community facilities capital expenditure relative to the corresponding annual budget adopted by Council	80%-110%	80%-110%	80%-110%
Transport	Percentage of transport capital expenditure relative to the corresponding annual budget adopted by Council	80%-100%	80%-100%	80%-100%
Waste Management	Percentage of waste minimisation & management capital expenditure relative to the corresponding annual budget adopted by Council	80%-100%	80%-100%	80%-100%
Property	Percentage of Property capital expenditure relative to the corresponding annual budget adopted by Council, for budgets under the control of the Property team.	80%-100%	80%-100%	80%-100%

Equity raise overview

Ratepayer Assistance Scheme

1. Equity required

\$35m meets the estimated equity requirement under the Base Case with a c.10% buffer - \$21m is required from councils

- The 2025 Base Case indicated an equity requirement of \$26.1m and to provide a comfort buffer the expected equity raise was indicatively set at \$30m - \$35m
- The refreshed Base Case equity requirement is estimated to be \$32.2m (to cover establishment costs ~\$15m and operating deficits ~\$17m)
- An equity ask of \$35m provides a ~10% buffer based on conservative Base Case assumptions
- There is a constraint on the investment of any single investor at 20% of total capital (to avoid the risk of RAS being on-balance sheet for that investor), so the maximum individual shareholders can take will be c.\$7m if the \$35m total equity raised
- Proposed equity contributions are outlined below:

	% contributed	Equity contribution (\$)
Central Government	20%	\$7m
LGFA	20%	\$7m
Councils	60%	\$21m
Total equity raised	100%	\$35m

- To align with LGFA's capital structure it is proposed that councils and LGFA also subscribe for uncalled capital of \$21m on a 1:1 basis with paid up capital

2. Council funding / equity

Committed councils funding will only be drawn down following the receipt of unconditional support from all stakeholders

- Before RAS establishment can formally commence, approval will be required from central government, LGFA and councils as:
 - Shareholders – to provide the necessary equity funding
 - Stakeholders (in addition to the equity) – i.e.:
 - Central Government – policy, supporting legislation, liquidity standby facility
 - LGFA – debt / treasury management, subscription to RAS debt and preference shares
 - Councils – agreement to make products available / RAS membership arrangements
- The explicit unconditional support of all three stakeholders is required before any council funding will be drawn down and spent
- Council funding will be provided to LGNZ, who will hold the funds on trust and will be reflected in equity in RAS in due course once it is incorporated
- Council's funding will be reflected in RAS equity (ie ordinary shares)
 - Ordinary shares will be issued at a price of \$1 per share
 - Ordinary shares receive one voting right per share
 - While there is no guarantee of performance, financial modelling based on various assumptions indicates RAS may provide a reasonable return on the equity invested
- ~\$4m in funding has already been provided by a group of Funding Councils and LGNZ and this funding and any further development funding provided (**Early Capital**) will count as establishment equity. In addition:
 - Early Capital will receive a preferential return to compensate the providers of that capital for the development risk taken
 - The return on the Early Capital will be repaid before any return is provided to the ordinary shareholders
 - Early capital will convert to ordinary capital on a 1:1 basis once all of the preferential return has been paid

3. Council contributions - LGFA insights

LGFA has 30 council shareholders who contributed \$20m paid-in capital

As at 30 June 2026	Paid in capital at establishment (\$)	Paid in capital at establishment (%)	Current paid in capital (\$)	Current paid in capital (%)
Minister of Finance and Minister for Local Government	5,000,000	20.0%	5,000,000	20.0%
Auckland Council	2,000,000	8.0%	1,865,980	7.5%
Christchurch City Council	2,000,000	8.0%	1,865,980	7.5%
Hamilton City Council	2,000,000	8.0%	1,865,980	7.5%
Bay of Plenty Regional Council	2,000,000	8.0%	1,865,979	7.5%
Greater Wellington Regional Council	2,000,000	8.0%	1,865,979	7.5%
Tasman District Council	2,000,000	8.0%	1,865,979	7.5%
Tauranga City Council	2,000,000	8.0%	1,865,979	7.5%
Wellington City Council	2,000,000	8.0%	1,865,979	7.5%
Western Bay of Plenty District Council	2,000,000	8.0%	1,865,979	7.5%
Whangarei District Council	800,000	3.2%	746,392	3.0%
Hastings District Council	400,000	1.6%	373,196	1.5%
Marlborough District Council	-	0.0%	200,000	0.8%
Selwyn District Council	200,000	0.8%	186,598	0.7%
Gisborne District Council	-	0.0%	100,000	0.4%
Hauraki District Council	-	0.0%	100,000	0.4%
Horowhenua District Council	-	0.0%	100,000	0.4%
Hutt City Council	-	0.0%	100,000	0.4%
Kapiti Coast District Council	-	0.0%	100,000	0.4%
Manawatu District Council	-	0.0%	100,000	0.4%
Masterton District Council	100,000	0.4%	100,000	0.4%
New Plymouth District Council	100,000	0.4%	100,000	0.4%
Otorohanga District Council	100,000	0.4%	100,000	0.4%
Palmerston North City Council	-	0.0%	100,000	0.4%
South Taranaki District Council	100,000	0.4%	100,000	0.4%
Taupo District Council	100,000	0.4%	100,000	0.4%
Thames - Coromandel District Council	-	0.0%	100,000	0.4%
Waimakariri District Council	-	0.0%	100,000	0.4%
Waipa District Council	100,000	0.4%	100,000	0.4%
Whakatane District Council	-	0.0%	100,000	0.4%
Whanganui District Council	-	0.0%	100,000	0.4%
Total	25,000,000	100%	25,000,000	100%

RAS Funding Council

30 council shareholders (18 at establishment) + Central Government

The 18 original council shareholders sold down to the other councils after two years

Central Government contributed \$5m (20% of paid in capital) but did not subscribe for unpaid capital

The largest council shareholders each contributed \$2m at establishment

Top ten councils contributed \$18.8m / c.75% of paid equity at establishment and 94% of council contributions

Bottom 20 councils have contributed \$2.5m (c.10%) of paid equity

Prior to the sell-down, "small" councils only contributed \$1.2m (c.5%)

LGFA equity capital comprises \$25m paid up capital + \$20m uncalled (pro rata to council paid up shareholdings)

4. Council contributions – Funding Councils

If Funding Councils provide funding pro rata an additional c.\$11m is required from the rest of the sector...

- All councils are being offered the opportunity to invest in RAS equity
- The actual amount invested by each council will depend on individual appetite
- The experience with LGFA is that:
 - Not all councils will contribute, so that those that do contribute will need to take more than their pro rata share
 - The large councils need to provide the majority of the funding (at establishment of the LGFA the top 10 provided 94% of council equity)

Council	2024 rates revenue (\$000)	2024 rates revenue (%)	Implied equity subscription (NZ\$)
Funding Councils			
Auckland (Group)	2,523,000	29%	6,049,681
Hamilton City	246,572	3%	591,233
Tauranga City	257,766	3%	618,075
New Plymouth District	132,257	2%	317,127
Palmerston North City	121,056	1%	290,270
Hutt City	156,488	2%	375,229
Wellington City	459,732	5%	1,102,351
Queenstown-Lakes District	123,066	1%	295,089
Sub-total	4,019,937	46%	9,639,055
All other councils			
All other councils	4,738,046	54%	11,360,945
Sub-total	4,738,046	54%	11,360,945
Total equity contribution	8,757,983	100%	21,000,000

5. Council contributions - Funding Councils (cont.)

Funding Councils will need to lead the \$21m in contributions required – minimum 2x pro rata contribution is proposed

- Auckland Council is capped at \$7m which is 1.2x its pro rata share
- The table below outlines a 2x pro rata contribution from the Funding Councils (and Christchurch, which has not been part of the Steering Group since 2022)
- It still requires the smaller councils to contribute \$3.5m (which, based on the LGFA experience, is likely to be challenging)

	Equity contribution to date (\$)¹	Remaining equity contribution (\$)	Total equity contribution (\$)	% contributed²	Contribution relative to pro rata share (x)
Auckland Council	\$0.77m	\$6.23m	\$7m	20%³	1.2x
Hamilton City	\$0.57m	\$0.63m	\$1.2m	3%	2.0x
Tauranga City	\$0.67m	\$0.53m	\$1.2m	4%	2.0x
New Plymouth District	\$0.30m	\$0.30m	\$0.6m	2%	2.0x
Palmerston North City	\$0.25m	\$0.35m	\$0.6m	2%	2.0x
Hutt City	\$0.20m	\$0.60m	\$0.8m	2%	2.0x
Wellington City	\$0.67m	\$1.53m	\$2.2m	6%	2.0x
Christchurch City	\$0.15m	\$3.15m	\$3.3m	9%	2.0x
Queenstown-Lakes District	\$0.20m	\$0.40m	\$0.6m	2%	2.0x
Total equity raised	\$3.78m	\$13.72m	\$17.5m	50%	
Other councils			\$3.5m	10%	
Total council equity			\$21m	60%	

6. 2027 LTP consultation

The 2027 LTP is the most efficient and effective way for councils to confirm their intentions in the required timeframes

- In order to confirm support from councils and be in a position to have RAS operational in 2028 the 2027 LTP is the optimal way for councils to consider RAS and obtain approval
- LTP consultation is required to:
 - Establish a CCO
 - Commit to contribute \$[x] equity (assuming consultation supports it)
 - Approve joining RAS as a member including signing up to a J&S guarantee
- To maximise efficiency for councils, LGNZ, LGFA, Cameron Partners and Simpson Grierson will provide the following support:
 - Attendance at council forums / workshops as appropriate
 - Providing draft council materials, including:
 - Generic council paper outlining details of RAS, and decisions sought
 - Generic LTP consultation materials and clauses for insertion
 - 2026 RAS business plan information (a refresh of the 2025 plan) including presenting the financial modelling assumptions and outputs with Q&A
 - Legal information pack (from Simpson Grierson), including:
 - Explanation of RAS equity securities and drawdown process
 - Indicative term sheets for RAS equity securities
 - Draft equity Funding Letter
 - Reliance letter

Important notice

The information in this document (the “Presentation” which expression includes the whole and any part of the Presentation and any other written or oral material provided in connection with it) regarding the proposed Ratepayers Assistance Scheme (“RAS”) has been prepared by Cameron Partners Limited (“Cameron Partners”), acting as financial adviser to Local Government New Zealand (“LGNZ”).

Cameron Partners has been authorised by LGNZ to dispatch this Presentation to members of the RAS Steering Group (“Recipients”). This Presentation is confidential. A Recipient may share this Presentation with the elected members, officers and professional advisers of the council it represents, for the purpose of that council considering the proposed RAS but otherwise must not disclose it to any other person without the prior written consent of LGNZ or Cameron Partners. Any disclosure by a Recipient is made at that Recipient’s own discretion and risk. Each Recipient is responsible for ensuring that any person to whom it discloses this Presentation is made aware of, and complies with, the terms of this Important Information section. Any person who receives this Presentation, directly or indirectly, from a Recipient does so on these terms, and LGNZ and Cameron Partners accept no responsibility or duty of care to any such person.

The use of this Presentation is subject in all respects to the terms and conditions set out below. By continuing to read, use or otherwise act on this Presentation, you agree to be bound by the terms and conditions set out in this Important Information section.

The information in this Presentation has been prepared from information provided by LGNZ and from publicly available sources. Cameron Partners has relied on that information and has assumed, without independent verification, that it is true, accurate, complete, and up to date as at the date of this Presentation. This Presentation has been prepared solely to assist Recipients in considering, and informing their respective councils about, whether to express an interest in participating in the proposed RAS. It is a summary only, and does not purport to be complete, and has not been audited or independently verified. Nothing in this Presentation constitutes a recommendation or advice by LGNZ or Cameron Partners. This Presentation must not be used for any purposes other than that for which it is supplied.

This Presentation is not, and is under no circumstances to be construed as, an offer of financial products for issue requiring disclosure to an investor under Part 3 of the Financial Markets Conduct Act 2013 (the “FMCA”). It is not been registered, filed with or approved by any New Zealand regulatory authority or under or in accordance with the FMCA. It is not a disclosure document under New Zealand law and does not contain all the information that a disclosure document is required to contain under New Zealand law.

Any prospective, pro forma or illustrative financial information contained in this Presentation is subject to known and unknown risks, economic and competitive uncertainties, and assumptions that may not prove to be correct. Accordingly, there can be no assurance that such results will be realised and any variance from actual results may be material. Recipients are cautioned not to place any reliance on any such information. Before making any decision in relation to the RAS, Recipients should consult with their own legal, tax, business and/or financial advisers. In no circumstances will Cameron Partners or LGNZ be responsible for any costs, losses, liabilities or expenses incurred in connection with any appraisal or investigation of the RAS or for any other costs, losses, liabilities or expenses incurred by any Recipient or any other person.

The information contained in this Presentation has been prepared in good faith and is the sole responsibility of LGNZ. To the maximum extent permitted by law, LGNZ and Cameron Partners, and each of their respective directors, officers, employees, agents and advisers (together, the “Relevant Persons”) disclaim all liability and responsibility (including without limitation any liability arising from fault or negligence on the part of any Relevant Person) for any direct or indirect loss or damage which may be suffered by any Recipient or any other person through use of or reliance on anything contained in, or omitted from, this Presentation. No representation or warranty, express or implied, is made by any Relevant Persons as to the accuracy, completeness, currency or reasonableness of the information in this Presentation, including any forecasts or projections.

Recipients acknowledge that this Presentation may be subject to the Local Government Official Information and Meetings Act 1987. If a Recipient, or any council to which it has disclosed this Presentation, receives a request for its release, or proposes to include it in any publicly available meeting material, the Recipient must ensure that LGNZ and/or Cameron Partners is consulted before doing so.

All information within this Presentation is believed to be current at the date this Presentation was dispatched. LGNZ and Cameron Partners are under no obligation to update this Presentation or correct any inaccuracy which may become apparent after that date. All dollar amounts are in New Zealand dollars unless otherwise stated. This Important Information section is governed by the laws of New Zealand



Contact

Auckland

Level 23 Vero Centre, 48 Shortland Street
PO Box 1277 Auckland, New Zealand
+64 9 912 8580

Wellington

Level 12, 171 Featherston Street
PO Box 10-307, Wellington, New Zealand
+64 4 499 6650

cameronpartners.co.nz

